


Les Transformations de Southport Phasing Plan Mar 25

Eastbank Street North Footpath
 Pedestrian diversion installed (access to buildings and Chapel St to be maintained)
 Removal of existing kerbs and footpath paving
 Installation of new concrete paving and granite sets along shop fronts



Phase 2 Pedestrian diversion route

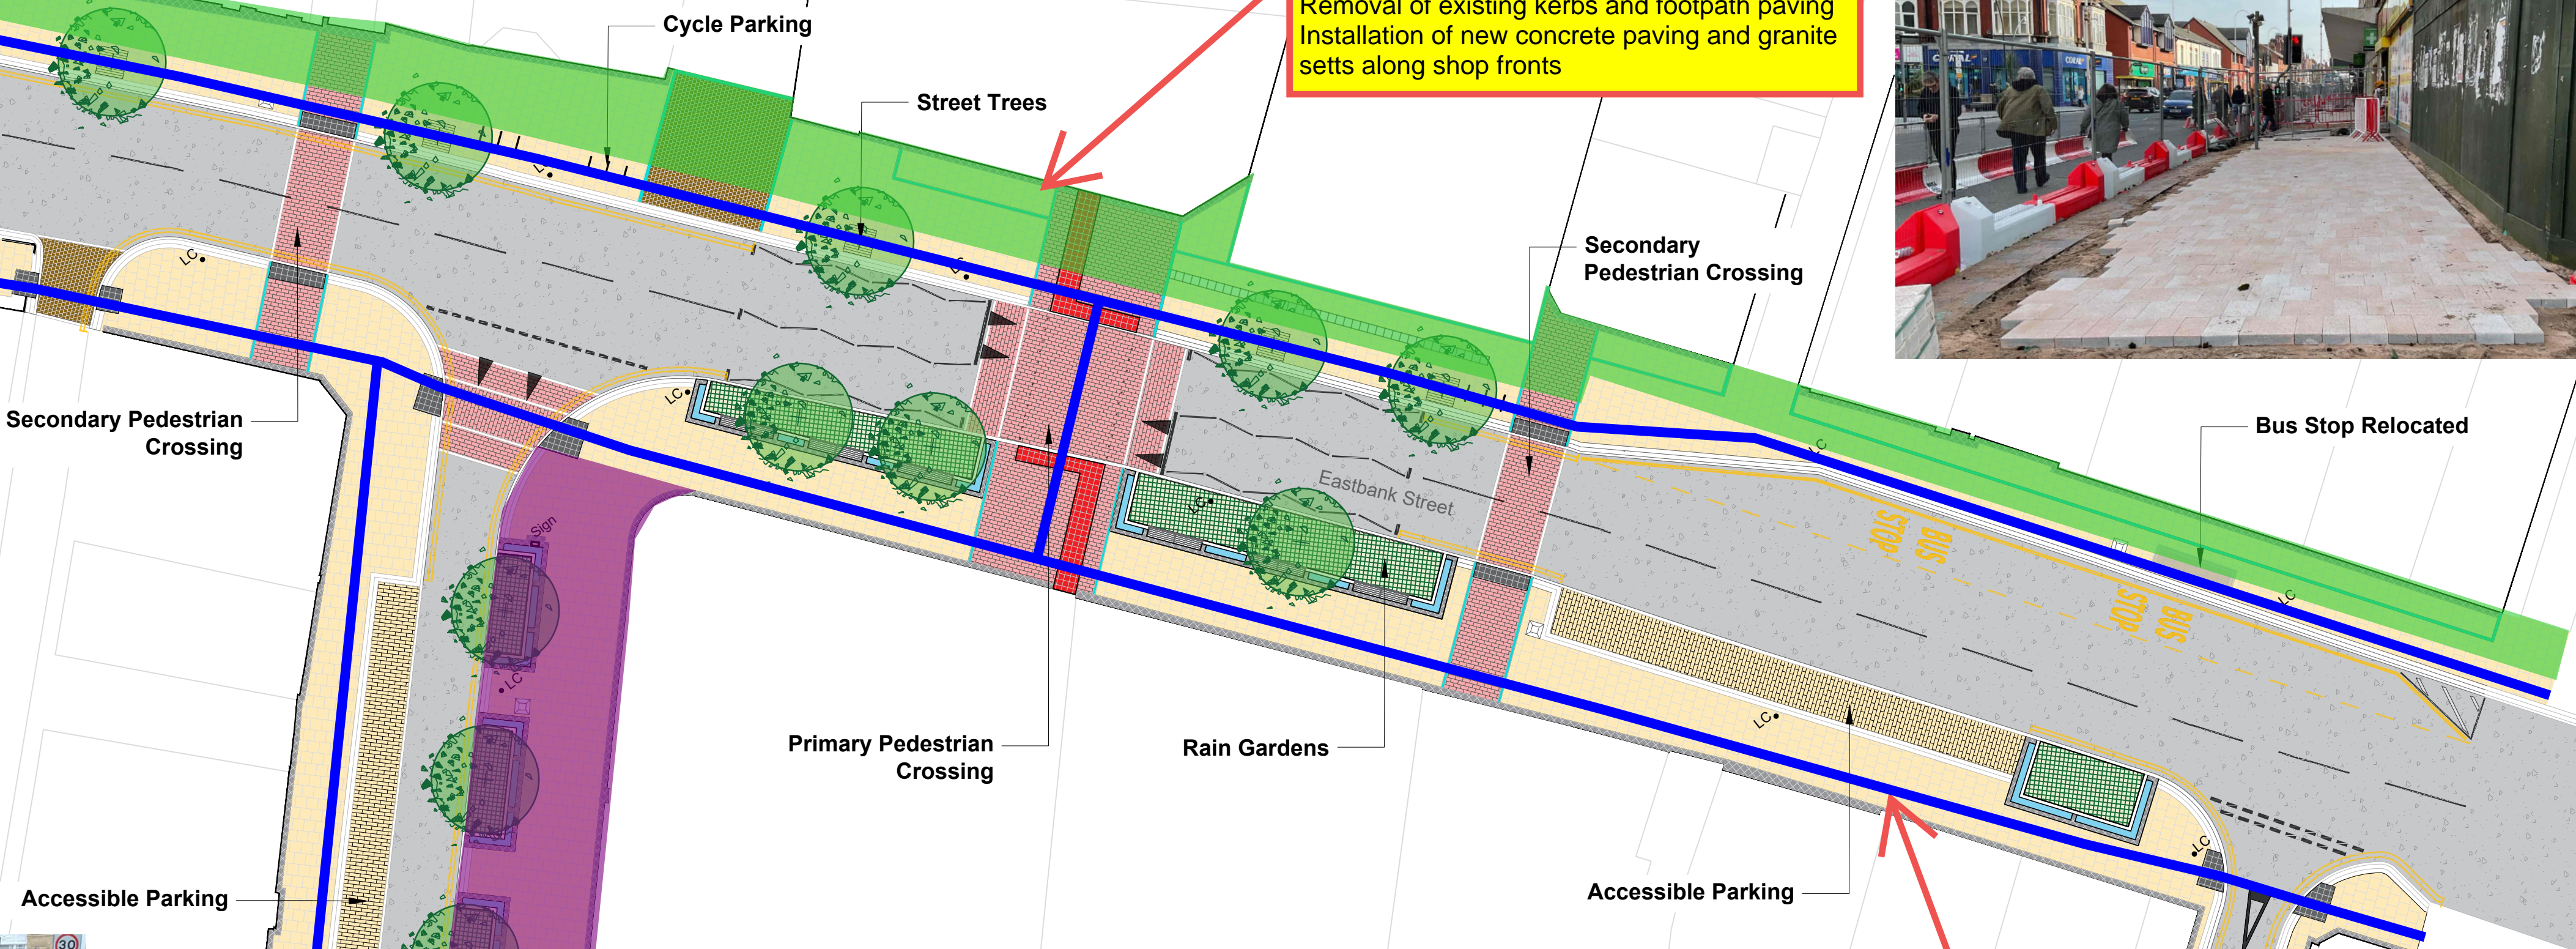

Bus Stop Relocated

King Street East Footpath and Carriageway
 Installation of new drainage system
 Installation of new concrete paving and granite sets



Eastbank Street South Footpath
 Pedestrian diversion removed
 Installation of recess chamber lids
 Grouting of sets adjacent to building

Market Street North Footpath and Carriageway
 Installation of 2no. tree pits
 Removal of existing kerbs and carriageway
 Installation of new permeable road
 Installation of new kerpline, concrete paving and granite sets

